

Project Planning Phase

Project Planning Template

Auto Ticket Classification using Flow Designer

Date	2 oct 2026
Team ID	SWTID-2026-5846
Project Name	Auto Ticket Classification using Flow Designer
Maximum Marks	5 Marks

1. Product Backlog, Sprint Schedule and Estimation

The backlog below translates the implemented project into Epics and User Stories. Story points follow the Fibonacci-style scale specified in the Planning Logic document.

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Points	Priority	Team Members
Sprint-1	Epic 1 – Requirement Analysis	USN-1	Document business use case and project requirements	2	Medium	Vimalraj Arul
Sprint-1	Epic 2 – Platform Configuration	USN-2	Create Project Update Set and make it current	1	Medium	Team Lead
Sprint-1	Epic 2 – Platform Configuration	USN-3	Create Incident WorkFlow custom table	3	High	Bala Chander
Sprint-1	Epic 2 – Platform Configuration	USN-4	Create fields and configure data types	3	High	Bala Chander
Sprint-1	Epic 2 – Platform Configuration	USN-5	Configure Category/Subcategory dependency	3	High	Bala Chander
Sprint-2	Epic 3 – Automation	USN-6	Create Auto Classify School IT Tickets flow	5	High	Murugan R
Sprint-2	Epic 3 – Automation	USN-7	Configure classification rules for issue types	3	High	Murugan R
Sprint-2	Epic 3 – Automation	USN-8	Configure caller email notification	2	Medium	Murugan R
Sprint-2	Epic 4 – Testing	USN-9	Execute classification and email test scenarios	5	High	Vimalraj Arul / Murugan R / Diwan Kumar M
Sprint-2	Epic 5 – Deployment	USN-10	Complete and export Project Update Set	2	Medium	Team Lead
Sprint-2	Epic 6 – Documentation	USN-11	Prepare documentation, screenshots and project evidence	3	High	Team

2. Sprint Tracker


The supplied template requires actual sprint dates and completed points. The source files do not provide your team's actual execution dates, so these fields are intentionally marked for entry rather than invented.

Sprint	Total Points	Duration	Start (Planned)	End (Planned)	Completed	Release (Actual)
Sprint-1	12	6 Days	[Enter actual]	[Enter actual]	[Enter actual]	[Enter actual]
Sprint-2	20	6 Days	[Enter actual]	[Enter actual]	[Enter actual]	[Enter actual]

3. Velocity

Using the planned backlog: 32 total story points / 2 planned sprints = 16 story points per sprint. Actual velocity should be recalculated from the completed-points column after the real sprint results are entered.

4. Planned Burndown

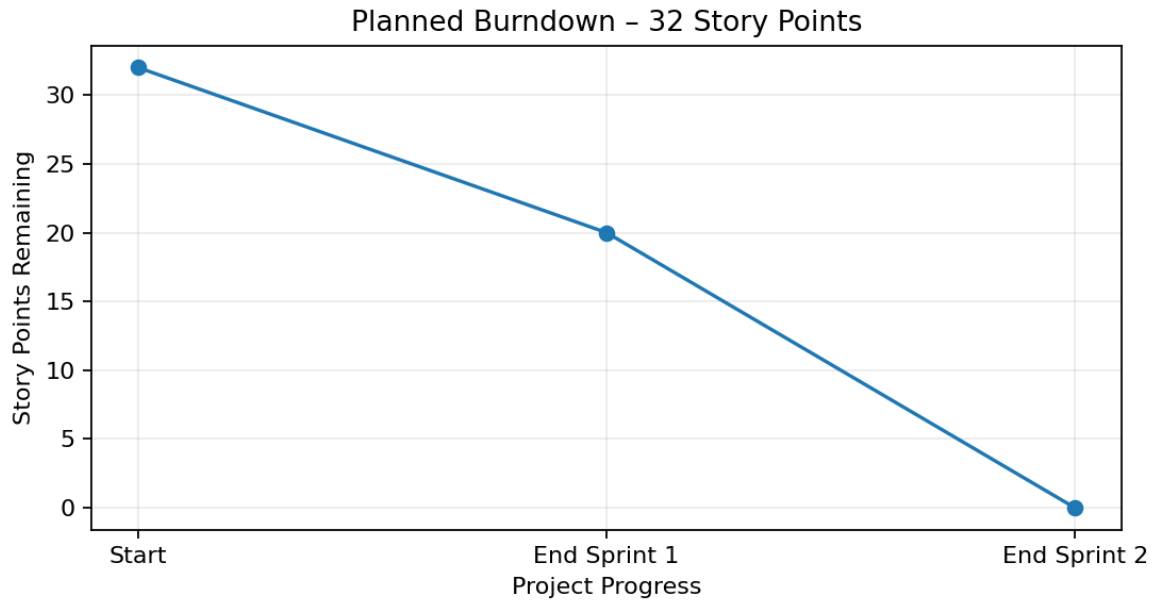

5. Sprint Deliverables

Sprint	Deliverables	Evidence
Sprint-1	Requirements, Update Set, custom table, fields and dependent choices	ServiceNow configuration screenshots
Sprint-2	Flow, classification, email, testing, deployment and documentation	Flow/test/email/Update Set evidence

6. Submission Notes

- Story points represent relative effort, not hours.
- Enter the team's actual sprint dates before submission.
- Enter actual Story Points Completed based on evidence.
- Use the actual release date for each sprint.
- Do not present the planning baseline as measured historical velocity.
